

Documentation 2

Week 2 Sprint 1

Candidate: 9, 15,17, 30,32,35,38

Fall, 2025

Contents

Day 1	2
Goals	6
Day 2-4	6
Day 5	7
Product Backlog	7
Time Log.....	8
Sprint Review:.....	8
Sprint Retrospective:.....	9
Goal	10
Minutes:	10

Day 1

We began the day with a meeting at 10:00, followed by a Q&A session where we were able to address several questions we had prepared in advance.

The main purpose of the meeting was to appoint a Scrum Master and establish a set of ground rules for our group of seven. Setting clear expectations early on was important to ensure better alignment, communication, and collaboration throughout the project.

Agreed-upon ground rules:

- Inform the group if you will be late to the daily meeting or need to leave earlier for the day.
- Prioritize open communication. If you are having a difficult day or struggling with a task, notify the group so that the team can assist or try to help you.
- Use Discord as the primary communication platform. GitHub and OneDrive will be used for sharing code and project documents.

These ground rules aim to reduce misunderstandings and support a positive and productive group dynamic.

We also agreed to meet at 10:00 each day, attend the Q&A session when necessary, and then hold our daily standup. Each daily meeting includes a brief recap of what each member accomplished the previous day, followed by outlining individual goals for the current day.

Any important issues or items requiring group decisions are discussed as needed.

Given that we are seven members, we decided to split into two subgroups: one focusing on backend development and the other on frontend development. This division was made to avoid overlap, reduce confusion, and ensure a clearer distribution of responsibilities.

After setting the group ground rules, we then move on to define our definition of done and acceptance criteria:

Definition of Done:

- The chatbot flow works in the prototype
- The user can complete all the intended steps
- The text is clear and free of major errors
- The team has tested it
- It has been reviewed by at least 2 teammates

- It meets the acceptance criteria
- It is added to the report (documentation/screenshots)

Acceptance Criteria:

- Chatbot asks for several required fields
- Chatbot confirms the information before continuing
- User can go back and correct mistakes
- Flow can be completed without external help

Then the GIT rules were next on the agenda, knowing that a lot of individuals would be working on the solution in parallel with each other. Git rules are shown below:

```
Rule 1: Never push directly to main. (This is reinforced on GitHub, but do not attempt)
• All new code must be integrated via Pull Request.

Rule 2: Use clear, descriptive branch names.
• Branch names should reflect work done on that branch.
-- frontend-<short-feature-description> : e.g. frontend-manualsetup-alignment-fix

Rule 3: Branch from main or latest relevant feature branch.
• Always create a new branch from latest, clean state of main (or relevant branch, i.e. frontend/backend)
• Example workflow: Create a descriptive branch from the existing frontend branch -> frontend-style-adjustments -> commit your changes -> create a pull request to merge frontend-style-adjustments with frontend.

Rule 4: Write meaningful commit messages.
• Commit descriptions should reflect changes made in that commit.
• Good: "Fixed manual input text field alignment", "fix: Resolved infinite loop in API client"
• Bad: "fixed summary", "improved descriptions"

Rule 5: Commit logical, complete code.
• Each commit should introduce one complete functional change.
• Avoid mixing multiple unrelated changes into a single commit.

Rule 6: Do not commit unfinished, untested or commented-out-code.
• Every commit should leave the project in a functional state. If this is not possible (due to e.g. time restraints), commit your current work to its related branch, but do not create a pull request.

Rule 7: When in doubt, branch out.
• If you are unsure what changes have been made or what state the project is in, create a new branch.

Refrain from merging your own changes if you have the ability to. Always get someone else to verify your merge. (Unsure if everyone can accept PRs or if only I can)
```

After aligning and agreeing upon the set of rules, we move on to Sprint planning in Scrumwise and brainstorming the different backlog items that would be needed to make the solution that we plan during the design process.

Optimize api prompt to lower token usage	2 points	Ready for sprint	
Upload for participant list: PDF/Word/CSV/Excel & img data extraction	2 points	Ready for sprint	
DB image handling	2 points	In progress	0%
Implement session id to maintain event creation	2 points	Ready for sprint	

A snippet of the backlog items views under the different Epics.

When we were done with listing the different must-do tasks, we started assigning rough estimate points. The points would be based on story point estimation, but also our opinion and how complex we thought the task itself would be.


Story Points Estimation



How much we know	Dependencies	How much work effort	Story Points
Everything	None	< 2 hours	1
Almost everything	Almost none	Half a day	2
Something	Some	Up to 2 days	3
Almost nothing	Few	Few days	5
Nothing	More than a few	Around a week	8 – must be split into smaller itens
Nothing	Unknown	More than a week	13 – must be split into smaller itens

Pick a row that represents your task best; if it fits more than one, pick the higher one.

We used Planning Poker via PlanningPokerOnline to ensure that individual opinions did not influence others during estimation. When there were significant differences in the assigned point values, we discussed to understand the reasoning behind each estimate before agreeing on a final value.



The backlog would end up looking like the figure shown below.

Technical Implementation related to Frontend			
	Epic	24 points	New
Standardize frontend formatting with shared css styles	2 points	New	
Finalize the landingsite	2 points	New	
Create post-registration user dashboard	3 points	New	
Edit button in summary list on AI setup page	1 point	New	
Ability to change scoring type in SetupAI and SetupManual (and dashboard)	2 points	New	
AI assistant on manual setup and home page	3 points	New	
Sponsor image upload for public card showcase and event image (also in SetupMethod.tsx and SetupSummary)	1 point	New	
Adjust scoring weights in setup based on selected scoring type	2 points	New	

After agreeing upon the items and the points, we went through the list and inserted items that were achievable and necessary for Sprint 1. The rest of the items that didn't get picked were further tasks that would be done in future sprints down the line. The snippet below shows the different items that were chosen and stored for future sprints.

Sprint 1	
Complete this sprint	In progress
PINE_H25	2.25 points behind
Deliver Sprint 1 assignment on Canvas	2 p To do
Standardize frontend formatting with shared css styles	2 p To do
Create post-registration user dashboard	3 p To do
Remove backendrequirements.txt from git	1 p To do
Text field issues in manual setup	1 p To do
FAQ "chatbot" widget	2 p To do
Decide later button logic separated from continue button	1 p To do
Adjust scoring weights in setup based on selected scoring type	2 p To do
Set up a DB	2 p To do
DB crud operations	2 p To do

Backlog items that are not assigned to any sprint	
Add correct descriptions for the different fields in the Rankin...	New
Visualize the preview alongside the setup page (not summary...	New
Ongoing/flexible AI assistant option from backend, need...	New
Add a backlog item	Showing 9 of 15 items
Technical Implementation related to Backend	
Improve AI Setup chat flow	New
General assistance AI logic/Q&A chatbot in landing page	2 points
Optimize api prompt to lower token usage	New
Upload for participant list: PDF/Word/CSV/Excel & img...	2 points
Implement session id to maintain event creation	New
Implement abuse protection	New
Upload for Event Info: PDF/Word/CSV/Excel & img data...	New
Nice to have: Async implementation between communication al...	New
Add a backlog item	Showing 8 of 14 items

Sprint 1 was activated, and everyone got to pick out tasks to work on, shown in snippet x as an example.

Frontend: Technical... Inspiration for post-registration dashboard and input for event format PINE_H25 1 point In progress 80%	Inspiration for post-registration dashboard and input for event format Guanyun 1 p 80%
Frontend: Technical... Create post-registration user dashboard PINE_H25 3 points In progress 67%	Create post-registration user dashboard Jakob 3 p 67%

Goals

The main goal for sprint 1 was set, and it was to get the basic functionalities and framework done for the solution, so that in sprint 2 we would implement the add-on functions.


The other goals:

- Make a database
- Connect the database with the AI agent
- Refactor the frontend code
- Improve pages on the front end, for example, the post-registration dashboard.


Day 2-4

The first day was primarily dedicated to planning the week ahead and discussing any issues that needed attention. The focus for the following days was to work through the backlog items on the task board and complete them within the expected timeframe.

Each day began with a short stand-up meeting where everyone provided a brief update on what they had accomplished the previous day and what they intended to work on next. This meeting also served as an opportunity to share any relevant information, address potential blockers, and ensure a common understanding of our overall progress, including our status in relation to the burndown chart.

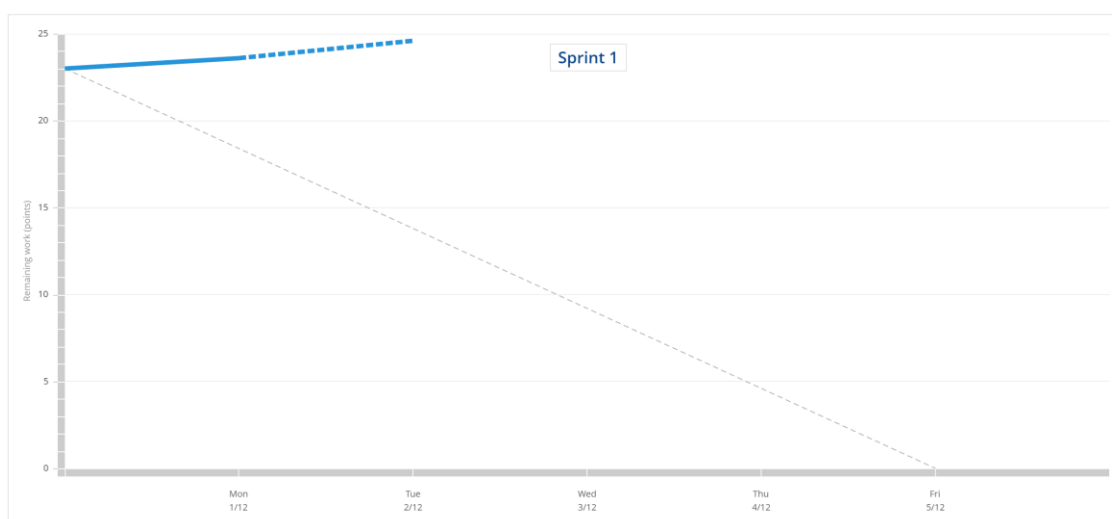

Burndown chart at the beginning of the week

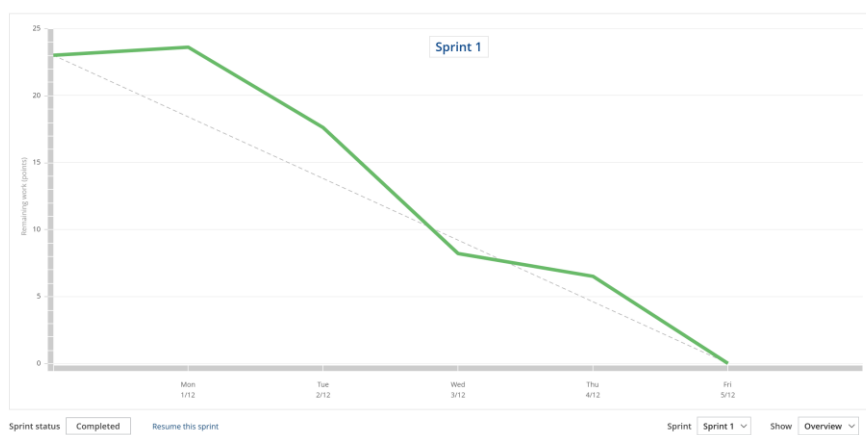

Burndown chart by the end of the week

Day 5

Product Backlog

Sprint 1				Resume this sprint	Completed
PINE_H25				29 points completed	
Shefat	4 p	Ranier	5 p	Jakob	6 p
Guanyun	1 p	Ola	7 p	Amund	4 p
Sprint Review & Retrospective - Sprint 1				2 p	Sprint completed
Write and deliver Sprint 1 assignment on Canvas				3 p	Sprint completed
Standardize frontend formatting with shared css styles				2 p	Sprint completed
Inspiration for post-registration dashboard and input for event format				1 p	Sprint completed
Create post-registration user dashboard				3 p	Sprint completed
Testing - Sprint 1				2 p	Sprint completed
Remove backend/requirements.txt from git				1 p	Sprint completed
Text field issues in manual setup				1 p	Sprint completed

FAQ "chatbot" widget		2 p	Sprint completed
Decide later button logic separated from continue button		1 p	Sprint completed
Adjust scoring weights in setup based on selected scoring type		2 p	Sprint completed
Set up a DB		2 p	Sprint completed
DB crud operations		2 p	Sprint completed
Choose an AI agent to use and implement it.		2 p	Sprint completed
Set up system prompt		1 p	Sprint completed
DB image handling		2 p	Sprint completed

Sprint 2	Start this sprint	In planning
PINE_H25	24 / 30 points	

Backlog items that are not assigned to any sprint	
Reporting & Testing	
Add a backlog item	
Showing 0 of 11 items	
Frontend: Technical Implementation	
Sponsor image upload for public card showcase...	
Ongoing/flexible AI assistant option from backen...	
Day/Night mode toggle	
Athlete registration (in dashboard?)	
Icons	
Change the Choose a "ranking" template to...	
"Decide later" setup page: update option for the...	
Add a backlog item	
Showing 7 of 24 items	
Backend: Technical Implementation	
Improve AI Setup chat flow	

"Decide later" setup page: update option for the...	
Add a backlog item	
Showing 7 of 24 items	
Backend: Technical Implementation	
Improve AI Setup chat flow	
Bug: changes to events should update and not create a...	
Optimize api prompt to lower token usage	
Upload for participant list: PDF/Word/CSV/Excel &...	
Implement session id to maintain event creation	
Implement abuse protection	
Upload for Event Info: PDF/Word/CSV/Excel & img...	
FK PK relationship between events and images tables...	
Nice to have: Async implementation between...	
Connect sideview on frontend to actual progress made...	
Add a backlog item	
Showing 10 of 16 items	

The overview shows the backlog items that were completed during Sprint 1 and the rest of the backlog items that are set up for the future sprints.

Time Log

The time log below shows the time usage on different tasks throughout the sprint.

Time used in this project

This project

All projects

Used by

Everybody

When

This month

Total 55 hours

Monday 1/12	Ranier	1 hour	In the backlog item "Write and deliver Sprint 1 assignment on Canvas"
Monday 1/12	Ola	2 hours	In the backlog item "Text field issues in manual setup"
Monday 1/12	Guanyun	1 hour	In the backlog item "Inspiration for post-registration dashboard and input for..."
Monday 1/12	Shefat	1 hour	In the backlog item "Remove backend/requirements.txt from git"
Tuesday 2/12	Ranier	1 hour	In the backlog item "Write and deliver Sprint 1 assignment on Canvas"
Tuesday 2/12	Jakob	1 hour	In the backlog item "Standardize frontend formatting with shared css styles"
Tuesday 2/12	Ola	2 hours	In the backlog item "Testing - Sprint 1"
Tuesday 2/12	Ranier	1 hour	In the backlog item "Decide later button logic separated from continue button"
Wednesday 3/12	Ranier	1 hour	In the backlog item "Write and deliver Sprint 1 assignment on Canvas"
Wednesday 3/12	Shefat	7 hours	In the backlog item "Set up a DB"
Wednesday 3/12	Hansim	5 hours	In the backlog item "Choose an AI agent to use and implement it."
Wednesday 3/12	Ranier	1 hour	In the backlog item "Sprint Review & Retrospective - Sprint 1"
Wednesday 3/12	Jakob	5 hours	In the backlog item "Create post-registration user dashboard"
Wednesday 3/12	Ranier	2 hours	In the backlog item "FAQ "chatbot" widget"
Wednesday 3/12	Guanyun	1 hour	In the backlog item "Inspiration for post-registration dashboard and input for..."
Wednesday 3/12	Guanyun	0.5 hours	In the backlog item "Inspiration for post-registration dashboard and input for..."
Wednesday 3/12	Shefat	2 hours	In the backlog item "Set up system prompt"
Wednesday 3/12	Shefat	8 hours	In the backlog item "DB crud operations"
Wednesday 3/12	Amund	2 hours	In the backlog item "DB image handling"
Thursday 4/12	Jakob	4 hours	In the backlog item "Create post-registration user dashboard"
Thursday 4/12	Ola	3 hours	In the backlog item "Adjust scoring weights in setup based on selected scoring..."
Thursday 4/12	Guanyun	0.5 hours	In the backlog item "Inspiration for post-registration dashboard and input for..."
Friday 5/12	Ranier	1 hour	In the backlog item "Write and deliver Sprint 1 assignment on Canvas"
Friday 5/12	Ranier	2 hours	In the backlog item "Sprint Review & Retrospective - Sprint 1"

Sprint Review:

During the Sprint Review, we invited one user to test the current state of our solution. Since the system has not yet been fully integrated, the user had to test the two components separately: the front-end flow and the AI agent.

Front-end feedback:

Most of the comments focused on clarity and detail. The user had difficulties understanding parts of the landing page and expressed uncertainty about how to proceed on certain screens. Although the overall navigation flow worked smoothly, there was a lack of clarity regarding what actions the user needed to take at specific points. The user also mentioned some inconsistencies in the colour choices used throughout the interface.

AI agent feedback:

While the AI agent showed some error-prone behavior, it successfully answered many of the user's questions. The user reported being satisfied with the interaction and even stated that they would prefer using this method compared to the manual process. One specific UX point raised was the need to scroll the entire page instead of having the chat contained in a scrollable box—this is something we will investigate further in the next sprint.

Conclusion:

Overall, many of the issues the user identified were backlog items we were already aware of and had planned to address in Sprint 2. The Sprint Review gave us confidence that we are progressing in the right direction, while also highlighting areas that require further improvement. There is still significant work ahead, but the feedback confirmed that our concept resonates well with users and is moving toward meeting their needs.

Sprint Retrospective:

After completing the sprint, the team held a retrospective to reflect on how we worked together and identify areas for improvement.

What we can improve:

One of the main points raised was that we were too cautious when selecting backlog items for the first sprint. We feared overestimating our capacity, which led us to choose fewer tasks than we could deliver. With uncertainty about how the process would unfold, we approached the sprint more defensively than necessary. As a result, we realized that we could have taken on a slightly larger workload.

Another improvement point was that some team members felt less involved than they would have liked. Even though everyone contributed where needed, we acknowledged the

importance of ensuring that every team member has tasks that match their availability and skills. Going forward, we will focus on distributing tasks more evenly so that everyone feels included throughout the sprint.

What went well:

Communication was one of the strongest aspects of the sprint. Whether through Discord or during in-person work sessions, the team kept each other updated and maintained clear dialogue throughout the process. You could also see the people felt more into their natural roles in the group, and the dynamic got better further into the sprint.

After a rocky start to the week, the team gradually became more consistent in using the Task Board. As everyone began updating their tasks more frequently, the workflow became clearer, and the Burndown Chart started to reflect our actual progress much more accurately as the sprint continued.

Additionally, establishing rules early—both general group rules and our Git workflow—helped prevent confusion or conflicts later. By aligning expectations from the start, we created a smoother and more predictable workflow, which contributed to a positive first sprint experience. Overall, the team felt that the sprint went as well as expected for our first week working together.

Goal

We successfully achieved the main goal for Sprint 1, which was to establish the basic framework for both the backend and the frontend.

With this foundation in place, we can now shift our focus toward integrating the two parts, resolving any bugs that arise, and continuing to add features that enhance the overall user experience. These will form the primary goals for the upcoming sprint.

Minutes:

Sprint planning: 5 hours

Sprint review: 1 hour

Sprint retrospective: 45 minutes
